INFINITY WEB & APPS

Infinity Studios Platform Production Delivery Plan

From the working demonstration to a live business: websites, admin panel and booking engine on AWS with live payments, a custom domain and secure storage, plus Android and iOS customer apps.

~12 weeks
to launch the websites and admin panel

~16 weeks
to publish the Android and iOS apps

+4 weeks
post-launch support (hypercare)

Prepared by
Infinity Web & Apps

Date
26 October 2026 · Version 1.0

Status
Proposal for discussion. Timelines and costs are estimates.

1 Summary

The demonstration already runs the complete booking platform: four customer websites, an admin panel and a shared booking, pricing and payment engine. The remaining work is mostly about **making it real**:

- Your content, prices and policies
- Production hosting on AWS with backups and monitoring
- Live payments and messaging
- Security and load testing
- A customer mobile app built on the same back end

Week 12	Week 15	Week 16	Weeks 13–16
Websites + admin live on your domain	Apps submitted to Google Play and the App Store	Apps live (subject to store review)	Hypercare: fixes and tuning after launch


Plan basis: a small dedicated team of 3–4 people (see section 4), React Native for the apps, and AWS Mumbai (ap-south-1) hosting. The overall range is **14–18 weeks** to full launch. The biggest factors outside our control are how quickly content and approvals arrive, Razorpay account activation, and app store review.

What is already built (working demo)

Area	What exists today	Status
Customer websites	Infinity Studios discovery site (search, categories, filters, service pages with live availability, booking, quotes with attachments, accounts, receipts), plus photography, podcast and events sites	Built
Admin panel	Dashboard, bookings, reschedule requests, enquiries and quotations, customers, payments and refunds, services, packages, locations, studio content, notification templates, roles, audit log	Built
Booking engine	Live availability, double-booking protection, payment holds, pricing with tax and deposits, status workflow	Built & tested
Payments	Razorpay checkout, server-side verification, refunds. Verified end to end in Razorpay *test mode*.	Test mode verified
API for the mobile app	Documented REST API (OpenAPI) with token sign-in, so the same API that serves the websites can serve the app	Ready
Hosting	Free demo hosting on Render: sleeps when idle, temporary file storage, no custom domain	Replace with AWS
Email / SMS / WhatsApp	Messages are built and logged as previews; no sending provider connected yet	To connect
Mobile app	Not started (API is ready for it)	To build

2 Timeline at a glance

Weeks run from project kick-off. Phases overlap because different team members work in parallel. ◆ = milestone.

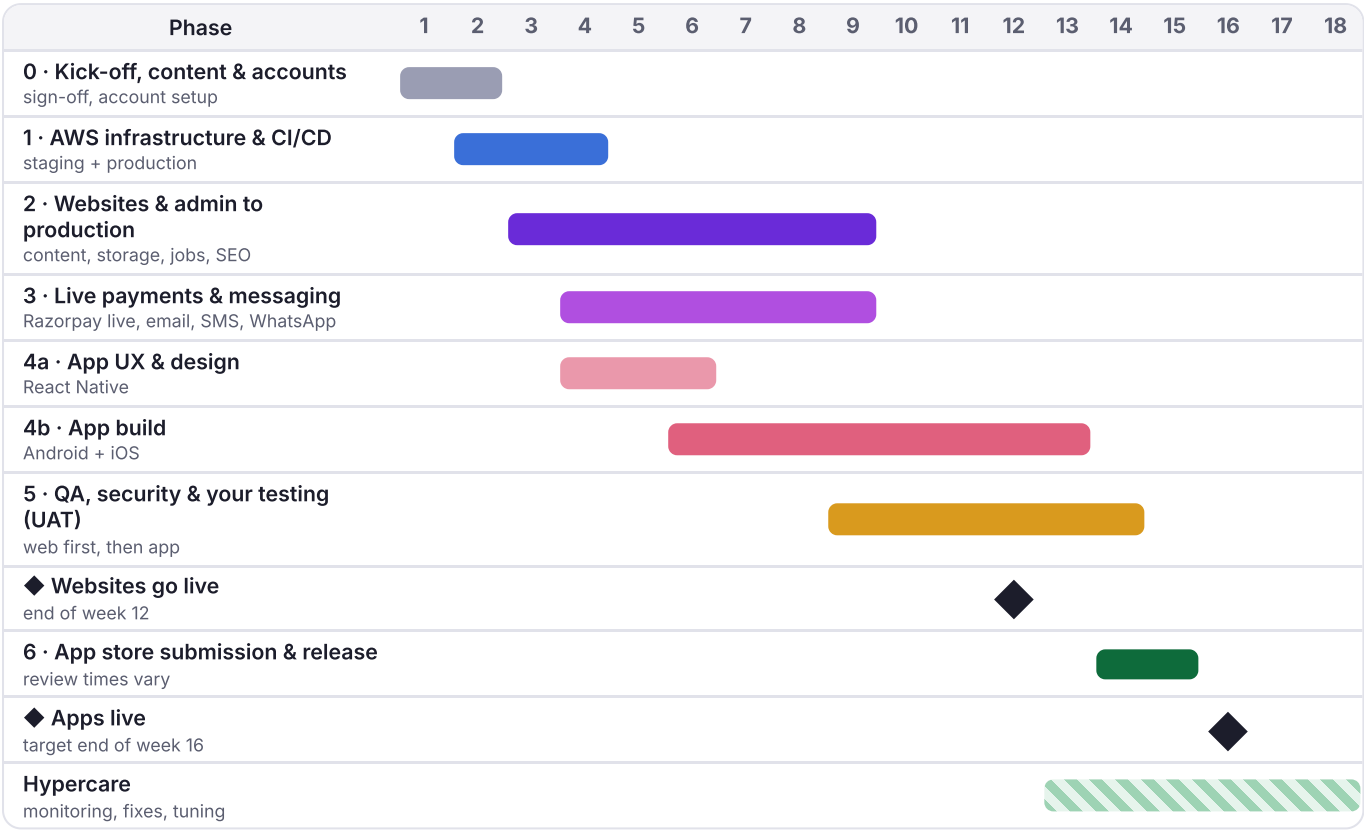

Key milestones

Week	Milestone	You will see
End of week 2	Scope, content plan and all accounts signed off	Confirmed plan; accounts created
End of week 4	Staging environment on AWS	A private staging link for review
End of week 8	Websites feature-complete with your content on staging	Full walkthrough with real services and prices
End of week 10	Live payments and messaging connected on staging	Real (small) test payment and confirmation emails
Week 11–12	Your acceptance testing (UAT) and go-live	Sites live on your domain
End of week 13	App beta on test devices	TestFlight (iOS) and internal testing (Android) builds
Week 15–16	Store submission and release	Apps on Google Play and the App Store

3 Phase-by-phase plan

Phase 0 · Kick-off, content & accounts

Weeks 1–2

WORK

- Confirm final scope, brand name, logo and colours
- Collect final services, packages, prices, GST treatment, deposit and cancellation/refund policy
- Collect studio addresses, opening hours, rooms and verified equipment
- Create or transfer accounts: AWS, domain, Razorpay, email sender, Google Play, Apple Developer

DONE WHEN

- Signed-off scope and content plan
- All accounts exist and we have access

Phase 1 · AWS infrastructure & deployment pipeline

Weeks 2–4

WORK

- Separate **staging** and **production** environments in AWS Mumbai
- Managed PostgreSQL database (Amazon RDS) with automated daily backups and point-in-time recovery
- Containers for the API, websites and admin (ECS Fargate) behind a load balancer
- S3 file storage for brief attachments and media, served through CloudFront CDN
- Domain and DNS (Route 53), free SSL certificates (ACM), secrets in AWS Secrets Manager
- Automatic deployments from GitHub (CI/CD), logs, uptime and error alerts (CloudWatch)

DONE WHEN

- Staging is reachable on a staging sub-domain
- One-click, repeatable deployments
- Restore from backup has been tested

Phase 2 · Websites & admin to production standard

Weeks 3–9

WORK

- Load your real content, images, services and prices; remove all demo labels
- Move file uploads to S3 (persistent, private, virus-scanned)
- Scheduled jobs: releasing expired payment holds, session reminders, follow-ups
- GST-compliant invoices (with your GSTIN and HSN/SAC codes)
- SEO (titles, sitemaps, search-engine indexing), analytics and cookie consent
- Final legal pages after your legal review; any agreed design refinements

DONE WHEN

- All pages show final content on staging
- Admin team trained on staging

Phase 3 · Live payments & messaging

Weeks 4–10

WORK

- Razorpay **live** keys after account activation (KYC), plus webhooks
- Refund rules that follow your approved cancellation policy
- Transactional email from your domain (e.g. Amazon SES), with SPF/DKIM/DMARC set up for deliverability
- SMS (requires Indian DLT registration of sender and templates) and WhatsApp Business templates, if wanted
- Google Maps on location pages (optional)

DONE WHEN

- A real low-value payment and refund succeed end to end
- Booking emails arrive from your domain

Phase 4 · Customer mobile app (React Native, Android + iOS)

Weeks 5–14

WORK

- **Design (weeks 5–7):** app flows and screens in the same discovery style as the website (home, search, categories, service detail, booking)
- **Build (weeks 7–14):**
  - sign-in and account; browse and search; live availability and booking
  - Razorpay in-app checkout; my bookings, reschedule and cancel; saved services; quote requests with photo upload
- Push notifications (Firebase / Apple) for confirmations and reminders
- Deep links from emails into the app; crash reporting

DONE WHEN

- Beta builds on test devices by week 13
- Feature-complete and store assets ready by week 14

The app uses the existing API and business rules, so availability, prices and bookings are identical on web and mobile.

Phase 5 · Quality, security & your acceptance testing

Weeks 10–15

WORK

- Full regression of the automated test suites; cross-browser and real-device testing
- Load testing for expected peak traffic; performance tuning
- Security review and penetration test; accessibility check
- Your team tests on staging (UAT); we fix agreed issues

DONE WHEN

- No open critical or high issues
- Your written go-live approval

Phase 6 · Launch & hypercare

Weeks 12–18

WORK

- **Week 12:** websites go live on your domain; data migrated from staging
- **Weeks 15–16:** app store submission, review and release
- **Hypercare (4 weeks from web launch, extended to cover the app release):** close monitoring, priority fixes and tuning

DONE WHEN

- Sites and apps live
- Handover documents and admin training complete

4 Team

Role	Responsibility	Allocation
Lead full-stack developer	API, booking engine, integrations, AWS set-up, technical decisions	Full time
Full-stack developer	Websites, admin panel, content migration, SEO	Full time
Mobile developer	React Native app for Android and iOS, store releases	Full time from week 5
QA & UI/UX designer	App design, test plans, regression and device testing	Part time

5 Production architecture on AWS

Customer-facing

- **Your domain** (e.g. yourbrand.in) via Route 53, with HTTPS everywhere (ACM)
- **CloudFront CDN** for fast images and pages across India
- **Websites + admin** (Next.js) on ECS Fargate
- **Mobile apps** on Google Play and the App Store, using the same API

Behind the scenes

- **API** (Node.js) on ECS Fargate behind a load balancer
- **PostgreSQL** on Amazon RDS: daily backups, point-in-time restore, encrypted
- **S3** for attachments and media (private by default)
- **Secrets Manager** for Razorpay and other keys (never in code)
- **CloudWatch** logs, metrics and alerts; scheduled jobs via EventBridge
- **SES** for email; Razorpay for payments; optional SMS/WhatsApp provider

Data stays in India: all hosting, database and file storage are in AWS Mumbai (ap-south-1). Card data never touches our servers; Razorpay handles it.

6 Estimated running costs

Estimates only. These are indicative figures for a typical launch-stage load, based on published list prices in October 2026. Actual costs depend on traffic, storage and the options chosen. We will confirm them with the AWS Pricing Calculator during Phase 1. Development fees are not included in this document.

Monthly AWS hosting (launch stage)

Item	Purpose	Est. per month (USD)
ECS Fargate	API, 4 websites and admin (small containers, 2 API instances)	$70 – $140
RDS PostgreSQL	Database with backups (Multi-AZ adds about 2× for high availability)	$35 – $120
Load balancer	Routes traffic to the containers	$20 – $30
NAT gateway / networking	Secure outbound access for private services	$35 – $50
S3 + CloudFront	File storage and CDN	$5 – $25
Route 53, Secrets Manager, CloudWatch, SES	DNS, key storage, monitoring, email	$10 – $30
Total	**Staging can run smaller or be paused to save cost**	**≈ $175 – $395** ≈ ₹15,000 – ₹33,000

Third-party and one-time costs

Item	Cost (indicative)	Notes
Razorpay payment gateway	Per-transaction fee (commonly around 2% on standard domestic plans) + GST on the fee	No monthly fee on standard plans; confirm your rate with Razorpay
Domain name	≈ ₹800 – ₹1,500 per year (.com / .in)	Premium names cost more
Apple Developer Program	US $99 per year	Needed to publish on the App Store
Google Play Console	US $25 one time	Needed to publish on Google Play
Email (Amazon SES)	≈ US $0.10 per 1,000 emails	Included in the AWS estimate at launch volumes
SMS / WhatsApp (optional)	Per-message charges set by the provider	SMS needs DLT registration (one-time fee set by the telecom operator)
Google Maps (optional)	Usage-based; low traffic usually stays within the free monthly usage	Only if you want maps on location pages
Penetration test (optional, recommended)	Quoted by the testing firm	One-off before launch

7 What we need from you, and when

The timeline assumes these arrive on time. Most delays on projects like this come from content and third-party approvals, not development.

Item	Needed by	Why it matters
Final brand name, logo, colours and domain choice	Week 1	Design and domain set-up start immediately
Services, packages, prices, GST details (GSTIN, HSN/SAC)	Week 2	Pricing engine and invoices
Deposit, cancellation and refund policy	Week 2	Payment and refund rules
Studio addresses, hours, rooms, verified equipment, photos	Week 3	Availability and content
AWS account (or permission for us to create one in your name)	Week 1	Infrastructure work starts in week 2
Razorpay account with KYC documents submitted	Week 2	Live-mode activation can take from a few days to a few weeks
Apple Developer account for your organisation	Week 4	Organisation enrolment needs a D-U-N-S number, which can take one to two weeks
Google Play Console account	Week 4	Identity verification for new accounts can take several days
Legal review of privacy policy and terms	Week 9	Required before go-live
Genuine client testimonials and portfolio (with permission)	Week 8	The site shows only real, authorised reviews
Named people for UAT and admin training	Week 10	Acceptance testing in weeks 11–12

8 Risks and how we manage them

Risk	Impact	How we manage it
Late content or approvals	Delays launch week for week	Content checklist with dates in week 1; staging lets you review as we go
Razorpay live activation takes longer	Payments stay in test mode	Submit KYC in week 1–2; the site can launch with "request booking" while activation completes
App store review rejection or delay	App release slips by days to a week	Follow store guidelines from day one; submit by week 15 to leave a buffer
Scope additions during the build	Longer timeline	Changes are agreed in writing with their time impact before work starts
SMS DLT registration delays	SMS starts later	Email and WhatsApp cover notifications until SMS is approved

9 Assumptions

- Scope is the platform as shown in the demo, plus the production items and mobile app described here. New features (for example memberships, multiple currencies, a staff mobile app or vendor marketplaces) are estimated separately.
- The customer app is a single React Native codebase for Android and iOS. A separate staff app is not included.
- One round of design revisions per screen set, and feedback on staging within 3 working days.
- Hosting costs are paid directly by you to AWS and the other providers, so you own all accounts and data.
- Week numbers count from the kick-off date agreed after sign-off.

Next steps

1. Review this plan and confirm scope.
2. Agree the kick-off date.
3. Start account set-up (AWS, Razorpay KYC, domain, Apple and Google developer accounts) so they are ready by week 2.

Prepared by Infinity Web & Apps · 26 October 2026 · Version 1.0. This document is a planning estimate, not a fixed quotation. Third-party prices and approval times are set by the respective providers and may change.
